
PRICE SCOPE: only the Nudura ICF formwork and associated accessories are included in our price. All other structure and information shown is supplied in good faith for coordination only and must be checked by the relevant professional.

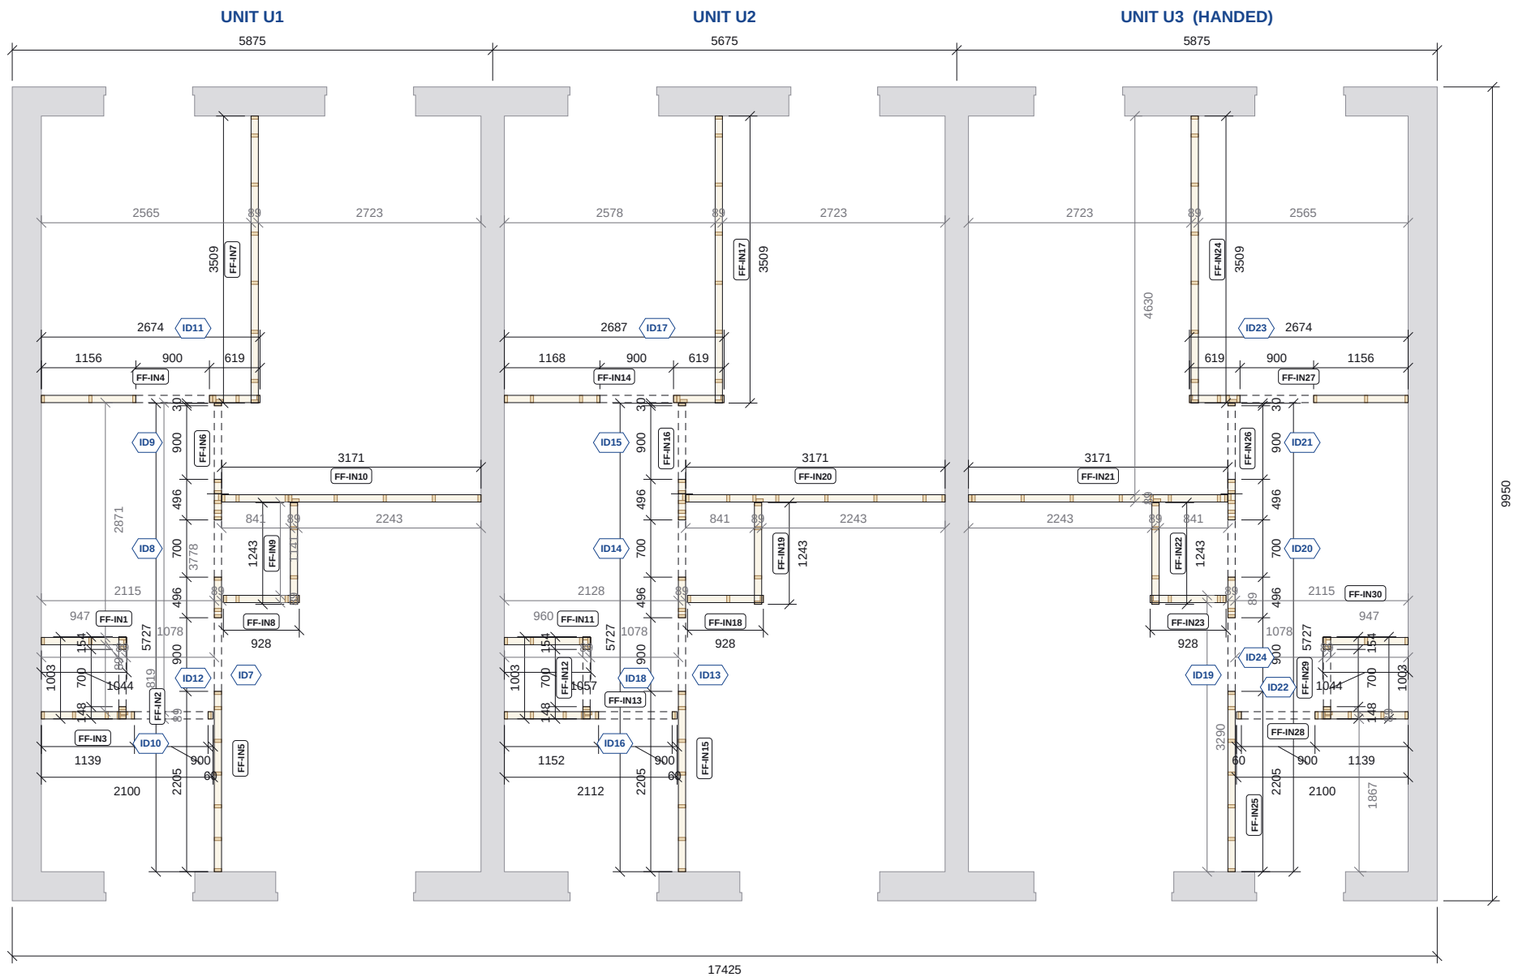

FIRST FLOOR TIMBER PARTITIONS PLAN

Scale 1:75 @ A3 | Plan cut at 1200 above floor level

Partition panel, studs cut at plan level | Panel joint | Nudura ICF shell (context only) | Door opening, head over

0 1 2 3 4 5m

QUOTATION - NOT FOR CONSTRUCTION

Do not scale. All dimensions in mm. Check all dimensions on site.

FIRST FLOOR SCHEDULES

PARTITION SCHEDULE

Panel	Unit	Studs	Use	Length	Doors
FF-IN1	U1	38x89 C16 @600	partition	1044	-
FF-IN2	U1	38x89 C16 @600	partition	1003	ID12
FF-IN3	U1	38x89 C16 @400	bathroom	2100	ID10
FF-IN4	U1	38x89 C16 @600	partition	2674	ID11
FF-IN5	U1	38x89 C16 @400	bathroom	4619	ID7, ID8
FF-IN6	U1	38x89 C16 @400	bathroom	1106	ID9
FF-IN7	U1	38x89 C16 @600	partition	3509	-
FF-IN8	U1	38x89 C16 @600	partition	928	-
FF-IN9	U1	38x89 C16 @600	partition	1243	-
FF-IN10	U1	38x89 C16 @600	partition	3171	-
FF-IN11	U2	38x89 C16 @600	partition	1057	-
FF-IN12	U2	38x89 C16 @600	partition	1003	ID18
FF-IN13	U2	38x89 C16 @400	bathroom	2112	ID16
FF-IN14	U2	38x89 C16 @600	partition	2687	ID17
FF-IN15	U2	38x89 C16 @400	bathroom	4619	ID13, ID14
FF-IN16	U2	38x89 C16 @400	bathroom	1106	ID15
FF-IN17	U2	38x89 C16 @600	partition	3509	-
FF-IN18	U2	38x89 C16 @600	partition	928	-
FF-IN19	U2	38x89 C16 @600	partition	1243	-
FF-IN20	U2	38x89 C16 @600	partition	3171	-
FF-IN21	U3	38x89 C16 @600	partition	3171	-
FF-IN22	U3	38x89 C16 @600	partition	1243	-
FF-IN23	U3	38x89 C16 @600	partition	928	-
FF-IN24	U3	38x89 C16 @600	partition	3509	-
FF-IN25	U3	38x89 C16 @400	bathroom	4619	ID19, ID20
FF-IN26	U3	38x89 C16 @400	bathroom	1106	ID21
FF-IN27	U3	38x89 C16 @600	partition	2674	ID23
FF-IN28	U3	38x89 C16 @400	bathroom	2100	ID22
FF-IN29	U3	38x89 C16 @600	partition	1003	ID24
FF-IN30	U3	38x89 C16 @600	partition	1044	-

Length = panel length along the wall (mm). Head and bottom rails as the studs. Bathroom walls at 400 centres for pattressing; riser boxing 38x47.

DOOR OPENING SCHEDULE

Label	Width	Height	Head	Label	Width	Height	Head
ID7	900	2100	2100	ID16	900	2100	2100
ID8	700	2100	2100	ID17	900	2100	2100
ID9	900	2100	2100	ID18	700	2100	2100
ID10	900	2100	2100	ID19	900	2100	2100
ID11	900	2100	2100	ID20	700	2100	2100
ID12	700	2100	2100	ID21	900	2100	2100
ID13	900	2100	2100	ID22	900	2100	2100
ID14	700	2100	2100	ID23	900	2100	2100
ID15	900	2100	2100	ID24	700	2100	2100

Structural opening sizes. Head level above underside of the bottom rail.

PARTITION TIMBER (THIS FLOOR, ALL UNITS)

Section	Pieces	Run m	4.8m lengths
38x89 C16	491	699.6	154
38x80 C16	3	7.8	2
30x89 C16	3	7.8	2

Studs, rails and noggins from the model. Order lengths = run / 4.8m +5%, not cut-optimised.

NOTES

1. Internal partitions only, non-load-bearing: 38x89 C16 studs at 600 centres with 38x89 C16 head and bottom rails; bathroom walls 38x89 C16 at 400 centres for pattressing; service riser boxing 38x47 C16 at 600. Panel marks refer to the partition schedule.
2. External, party and core walls are Nudura ICF (grey), shown for context only: read with the ICF drawings. Partitions are set out from the ICF internal face and adjacent partitions (grey set-out strings).
3. Door openings are structural opening sizes. Head level above underside of the bottom rail.
4. All units of the block shown (U1 left, seen from the front); the right-hand unit is handed. Dimensions to timber frame faces. Check all dimensions on site.

REVISIONS

REV	DATE	DESCRIPTION
Q01	19.10.26	First issue

Nudura™ BuildEase

CLIENT	PROJECT
Wannop Developments Ltd	Land to Rear of 1-8 Wesley Terrace, Castleside

DRAWING TITLE

T01 TERRACE OF 3 - FIRST FLOOR TIMBER PARTITIONS

Internal stud partitions, panels and door openings

SCALE	SIZE	DATE
1:75	A3	19.10.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-080-TF-04	Q01
